

DISTRIBUTION SHEET

To Distribution	From G. A. Barnes	Page 1 of 1 Date August 23, 1994
Project Title/Work Order WHC-SD-WM-TP-265, Test Plan for Enraf Series 854 Level Gauge Testing in Tank 241-S-106		EDT No. 604965 ECN No.

Name	MSIN	Text With All Attach.	Text Only	Attach./Appendix Only	EDT/ECN Only
R. P. Anantatmula	R1-30	X			
D. A. Barnes	R1-51	X			
G. A. Barnes	H5-09	X			
J. R. Biggs	T4-01	X			
D. C. Board	S1-57	X			
W. G. Brown	S2-45	X			
J. H. Huber	R1-49	X			
T. L. Moore	H5-09	X			
R. Ni	S5-07	X			
S. G. Pitman	P8-44	X			
R. S. Popielarczyk	R1-30	X			
R. E. Raymond	R2-54	X			
S. H. Rifaey	S2-45	X			
J. S. Schofield	R1-67	X			
C. P. Schroeder	L7-06	X			
W. F. White	L7-06	X			
J. H. Wicks	T4-08	X			
OSTI (2)	L8-04	X			

MASTER

DISCLAIMER

Portions of this document may be illegible in electronic image products. Images are produced from the best available original document.

5

sta 4
AUG 25 1994

ENGINEERING DATA TRANSMITTAL

2. To: (Receiving Organization) Distribution	3. From: (Originating Organization) Mechanical Equipment	4. Related EDT No.: NA
5. Proj./Prog./Dept./Div.: TWRS/Mechanical Equipment	6. Cog. Engr.: G. A. Barnes	7. Purchase Order No.: NA
8. Originator Remarks: Transmitted for release.		9. Equip./Component No.: NA
		10. System/Bldg./Facility: 241-S
11. Receiver Remarks:		12. Major Assm. Dwg. No.: NA
		13. Permit/Permit Application No.: NA
		14. Required Response Date: August 23, 1994

15. DATA TRANSMITTED					(F)	(G)	(H)	(I)
(A) Item No.	(B) Document/Drawing No.	(C) Sheet No.	(D) Rev. No.	(E) Title or Description of Data Transmitted	Approval Designator	Reason for Transmittal	Originator Disposition	Receiver Disposition
1	WHC-SD-WM-TP-265	A11	0	Test Plan for Enraf Series 854 Level Gauge Testing in Tank 241-S-106	Q	I	I	

16. KEY					
Approval Designator (F)		Reason for Transmittal (G)		Disposition (H) & (I)	
E, S, Q, D or N/A (see WHC-CM-3-5, Sec.12.7)		1. Approval	4. Review	1. Approved	4. Reviewed no/comment
		2. Release	5. Post-Review	2. Approved w/comment	5. Reviewed w/comment
		3. Information	6. Dist. (Receipt Acknow. Required)	3. Disapproved w/comment	6. Receipt acknowledged

17. SIGNATURE/DISTRIBUTION (See Approval Designator for required signatures)										(G)	(H)
Reason	Disp.	(J) Name	(K) Signature	(L) Date	(M) MSIN	(J) Name	(K) Signature	(L) Date	(M) MSIN	Reason	Disp.
1	/	Cog. Eng. GA Barnes	<i>J. Barnes</i>	8/24/94	H5-09						
1	/	Cog. Mgr. TL Moore	<i>T. Moore</i>	8/23/94	H5-09						
1	/	QA DC Board	<i>Don Board</i>	8/29/94	S1-57						
		Safety									
		Env.									
1	/	JR Biggs	<i>J. Biggs</i>	8-23-94	T4-01						
1	/	RE Raymond	<i>R. Raymond</i>	8/25/94	R2-54						

18. G. A. Barnes Signature of EDT Originator	19. J. R. Biggs Authorized Representative for Receiving Organization	20. T. L. Moore Cognizant Manager	21. DOE APPROVAL (if required) Ctrl. No. <input type="checkbox"/> Approved <input type="checkbox"/> Approved w/comments <input type="checkbox"/> Disapproved w/comments
---	---	--------------------------------------	---

RELEASE AUTHORIZATION

Document Number: WHC-SD-WM-TP-265 REV. 0

Document Title: TEST PLAN FOR ENRAF SERIES 854 LEVEL GAUGE TESTING
IN TANK 241-S-106

Release Date: 8/24/94

* * * * *

**This document was reviewed following the
procedures described in WHC-CM-3-4 and is:**

APPROVED FOR PUBLIC RELEASE

* * * * *

WHC Information Release Administration Specialist:



N. L. Solis

(Signature)

8/24/94

(Date)

SUPPORTING DOCUMENT

1. Total Pages 510 *23681254*

2. Title Test Plan for Enraf Series 854 Level Gauge Testing in Tank 241-S-106	3. Number WHC-SD-WM-TP-265	4. Rev No. 0
--	-------------------------------	-----------------

5. Key Words Enraf, level gauge, LIT APPROVED FOR PUBLIC RELEASE <i>8/24/94 D. White</i>	6. Author Name: G. A. Barnes <i>[Signature]</i> Signature Organization/Charge Code 7EA30/N3064
--	--

7. Abstract
This document details a plan to test an Enraf level gauge in tank 241-S-106.

8. ~~PURPOSE AND USE OF DOCUMENT - This document was prepared for use within the U.S. Department of Energy and its contractors. It is to be used only to perform, direct, or integrate work under U.S. Department of Energy contracts. This document is not approved for public release until reviewed.~~

~~PATENT STATUS - This document copy, since it is transmitted in advance of patent clearance, is made available in confidence solely for use in performance of work under contracts with the U.S. Department of Energy. This document is not to be published nor its contents otherwise disseminated or used for purposes other than specified above before patent approval for such release or use has been secured, upon request, from the Patent Counsel, U.S. Department of Energy Field Office, Richland, WA.~~

DISCLAIMER - This report was prepared as an account of work sponsored by an agency of the United States Government. Neither the United States Government nor any agency thereof, nor any of their employees, nor any of their contractors, subcontractors or their employees, makes any warranty, express or implied, or assumes any legal liability or responsibility for the accuracy, completeness, or any third party's use or the results of such use of any information, apparatus, product, or process disclosed, or represents that its use would not infringe privately owned rights. Reference herein to any specific commercial product, process, or service by trade name, trademark, manufacturer, or otherwise, does not necessarily constitute or imply its endorsement, recommendation, or favoring by the United States Government or any agency thereof or its contractors or subcontractors. The views and opinions of authors expressed herein do not necessarily state or reflect those of the United States Government or any agency thereof.

10. RELEASE STAMP

OFFICIAL RELEASE **5**
BY WHC
DATE AUG 25 1994
Ator 4

9. Impact Level Q

MASTER

**WHC-SD-WM-TP-265
Revision 0**

**Test Plan for
Enraf Series 854
Level Gauge Testing
In Tank 241-S-106**

**G.A. Barnes
Mechanical Equipment**

August 23, 1994

TABLE OF CONTENTS

	<u>Page</u>
1.0 INTRODUCTION	1
2.0 OBJECTIVE	1
3.0 SCOPE	1
4.0 TEST PROCEDURE	1
5.0 SAFETY	2
6.0 ORGANIZATION AND FUNCTIONAL RESPONSIBILITIES	2
7.0 REFERENCES	2
APPENDIX A	3

1.0 INTRODUCTION

An Enraf¹ Series 854 level gauge was installed on tank 241-S-106 (S-106) during the first week of June 1994. On August 11, 1994, the gauge's measuring wire broke. An investigation has been started to determine how the wire broke. This test plan identifies a qualification test that is part of this investigation.

2.0 OBJECTIVE

This is a qualification test to verify the design adequacy of the Enraf 854's stainless steel measuring wire in tank S-106. This test will also provide evidence as to the location and extent of potential corrosion on the measuring wire due to tank environment. The results from this testing will provide data for better material selections.

Even though the unit will be tested in an operational system, this test is not a Process Test as defined in WHC-IP-0842, Sect. 8.10 and EP 4.2 because changes are not being made to process operating parameters. The Enraf gauge will be operated by previously approved procedures. Also, no design changes are being made to the Enraf gauge or facility.

3.0 SCOPE

This test will involve placing the existing Enraf Series 854 level gauge back into service with the same type of measuring wire (316 stainless steel) that originally broke on August 11, 1994. The gauge will be operated for 14 days. At the end of the 14-day test, the wire shall be sent to Pacific Northwest Laboratory (PNL) for analysis.

4.0 TEST PROCEDURE

This test plan shall be inserted into the appropriate Job Control System work package for test execution.

All work performed on the Enraf Series 854 level gauge during this testing shall be performed in accordance with Tank Farm Maintenance Procedure 6-TF-125.

- 4.1 Remove the wire drum and displacer from the Enraf Series 854 level gauge installed on tank S-106. Thoroughly clean approximately the first 20 feet of measuring wire and the displacer with alcohol.
- 4.2 Reinstall the wire drum and displacer.
- 4.3 Start the Enraf level gauge.

¹Enraf, Inc.

- 4.4 Tank Farm Operations shall monitor and record the tank liquid level per TF-OR-WST-01-D on a daily basis.
- 4.5 At the end of 14 days of operation, remove the wire drum from the level gauge and send it to PNL for analysis (PNL contact-S. G. Pitman).

5.0 SAFETY

There is no anticipated safety impact with this testing (see Appendix A for Unreviewed Safety Question Screening).

6.0 QUALITY ASSURANCE

Quality Assurance will not be required to witness any part of the testing.

7.0 ORGANIZATION AND FUNCTIONAL RESPONSIBILITIES

Tank Farm Operations is responsible for providing a Person In Charge (PIC). The PIC will also be the Test Director.

Tank Farm Maintenance is responsible for operating the level gauge during the testing.

PNL is responsible for analyzing the measuring wire and writing an analysis report. Formal PNL guidance on analysis scope, criteria and controls will be forthcoming in a Letter of Instruction (LOI)

8.0 REFERENCES

- Enraf Series 854 ATG Level Gauge, Instruction Manual, Part No. 4416.220, Version 2.1.
- H-2-817634, INSTM ENRAF NONIUS ASSY INSTALLATION & RISER SCHED, SHEETS 1 and 2.
- 6-TF-125, Enraf Nonius Model 854 Level Gauge Preventive Maintenance and Calibration.

WHC-SD-WM-TP-265
Rev. 0

APPENDIX A

USQ Tracking Number: TF-94-0299, Rev. 0

Page 2¹ of 4

WHC-SD-WM-TP-265
REV. 0
PAGE 4

Does the PROPOSED CHANGE:

- A. Represent a change to the facility as described in the AUTHORIZATION BASIS documentation?
- | | | |
|----|---|-----------|
| NO | X | YES/MAYBE |
|----|---|-----------|

BASIS: The authorization basis for tank farms is the *Hanford Site Tank Farm Facilities Interim Safety Basis*, WHC-SD-WM-ISB-001, Rev. 0-C. The U.S. Department of Energy has authorized the use of the material in Chapter 6 for Safety Screenings and Safety Evaluations. Chapter 6 of WHC-SD-WM-ISB-001 refers the reader to the *Single-Shell Tank Interim Operational Safety Requirements*, WHC-SD-WM-OSR-005, Rev. 0. The availability of a functioning level monitoring system is required by LCO 3.1.1. If the primary waste level monitoring system in a non-interim isolated tank is inoperable, then tank farm operations has 14 days from discovery of the failure to restore the system to operable status.

The new Enraf level displacement gauge in tank 241-S-106 has been found to be non-functional. The plummet and a portion of the 316 stainless steel wire is missing (see Figure 1). The cause of the failure has not been determined conclusively. However, it is thought that the polyvinyl chloride riser liner is degrading and forming hydrochloric acid that runs down the 316 stainless steel wire and this caused the failure. The question at hand is does the loss of the plummet and the potential for another loss in the future cause hazards that are not addressed in the existing safety basis.

USA Tracking Number: TF-94-0299, Rev. 0

Page 3 of 4

WHC-SD-WM-TP-265 Rev. C
Page 6

D. Does the change impact:

- Implemented OSRs or IOSRs? NA NO X YES/MAYBE
- Approved IOSR Compliance Implementation Plans? NA X NO YES/MAYBE

BASIS: There already exists a requirement to measure the waste level in single-shell tanks. No new OSRs or IOSRs are required. Additionally, there is not an approved IOSR Compliance Implementation Plan for single-shell tanks at this time.

USQE #1

R. J. Van Vleet, Ph.D.

USQE #2

R. L. Guthrie

Print Name

R. J. Van Vleet 08/25/1994

Signature

Date

Print Name

R. L. Guthrie 8/25/94

Signature

Date

USO Tracking Number: TF-94-0299, Rev. 0

Page 4 of 4

WHC-SD-WM-ETP-265
Rev. 0 Page 7

WHC-SD-WM-ETP-016
Revision 0
Page 6

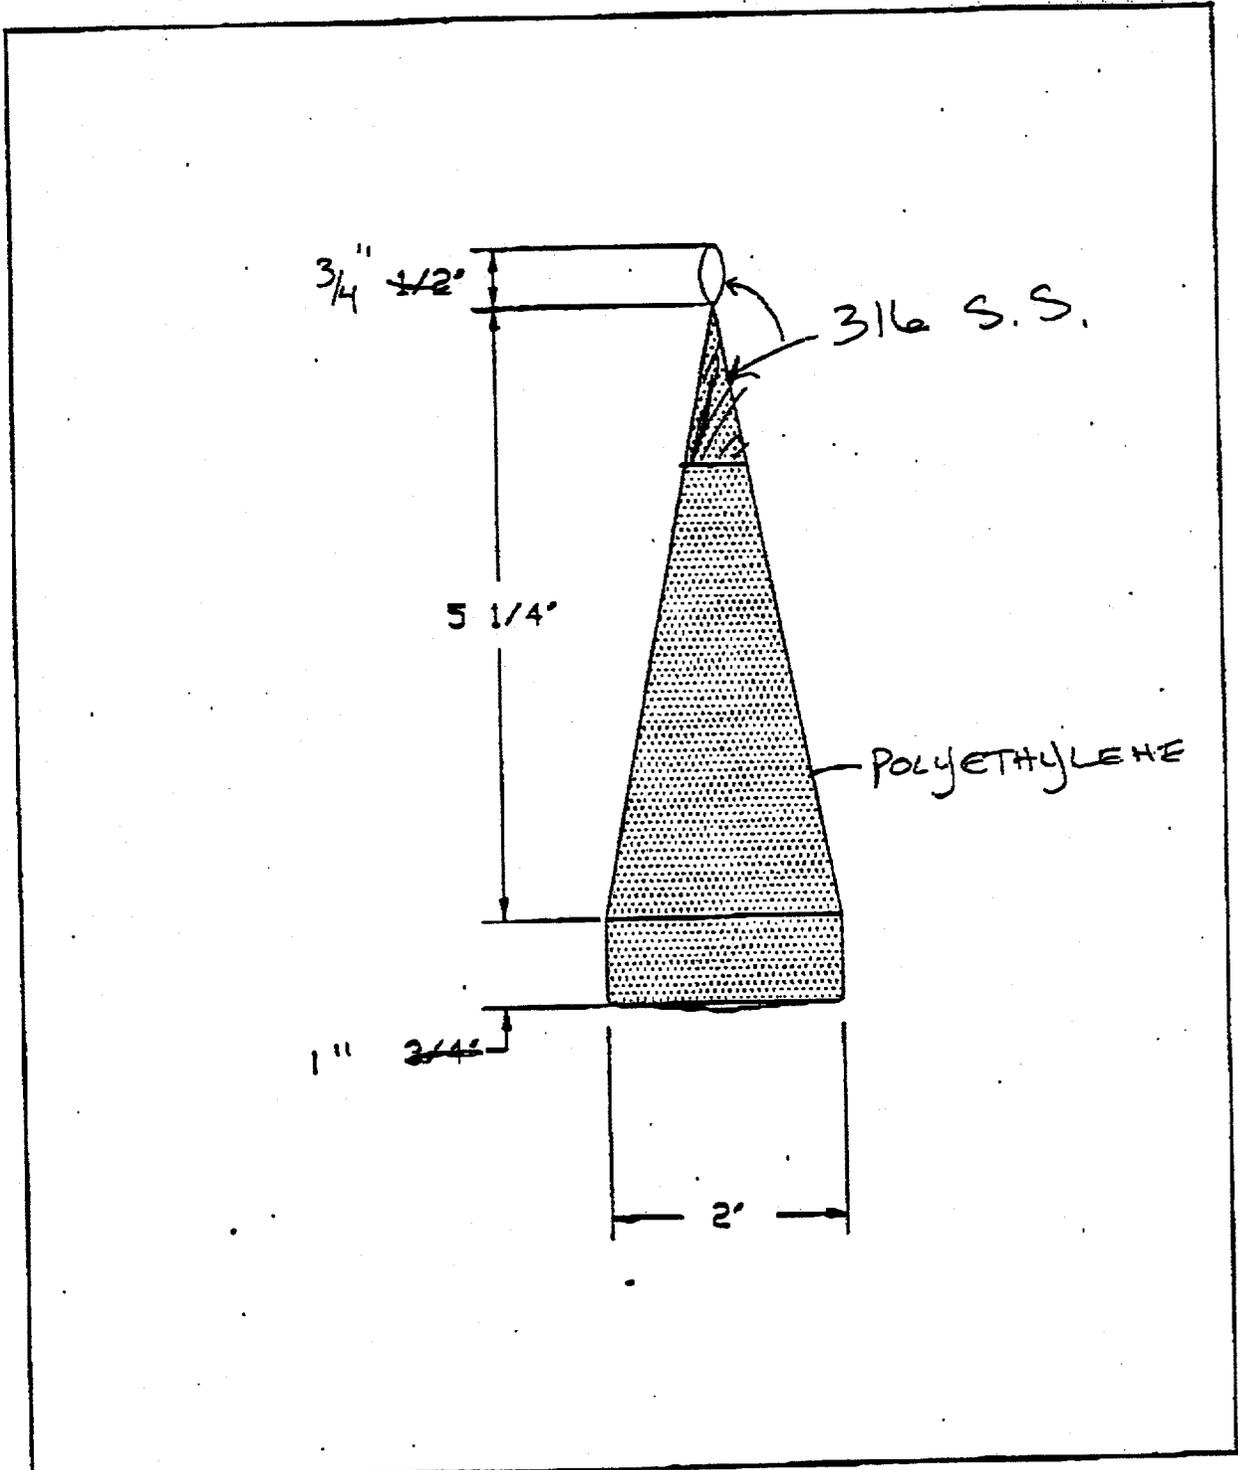


Figure 1 - LEVEL SENSOR PROBE
